



MOONDAO TOWN HALL · 8 OCTOBER 2026

Executive Branch Final Report

Q2 2026 – Q3 2026 · MDP-249 · Project #131

Pablo Moncada-Larrotiz Executive Lead

Ryan Communications, community & partnerships

Miguel Frontend & product engineering

Grades shown are provisional, for Executive Lead review



MDP-249: three objectives, five months, \$132k

1

Frank & DePrize

Secure a seat for Frank, or deploy DePrize with the Frank White capital, and launch a competitive lunar simulation and prototyping initiative.

2

Grow the network

Citizens 199 → 300, Teams 20 → 30, 60% of Teams using jobs or the marketplace, discovery calls with 15+ Teams.

3

Run the DAO well

Budget discipline, new project system, operational audit, for-profit plan, Realistic Goals, GDPR, an Executive Branch election.

PASSED 26 MAY

91% · 21 voters

FUNDED

1 May – 3 Sep 2026

CORE BUDGET

\$132,000

BONUS POOL

\$24,000 at risk

The term in six numbers

Live

DePrize on Arbitrum

Mainnet 25 Aug · 5 competitions on mainnet, 8 on Sepolia

+33%

Citizens

199 → 265 minted · 238 active (target 300)

20 → 25

Teams

Five new Teams, all active (target 30)

44%

Teams using services

11 of 25 posted a job or listing (target 60%)

\$132.7k

Spent vs \$132k budget

Within 0.6% · payroll via LlamaPay streams

359

Merged pull requests

Three-person team · 1 May – 7 Oct

DePrize is live on Arbitrum

25 AUG



Mainnet launch

DePrize #1: The Moon Is A Harsh Mistress (demo prize)

11 SEP



Security fix

Bug H-01 found in review, fixed and redeployed before any race

18 SEP



Full lifecycle

Sepolia: bet, declare winner, redeem, end to end

26 SEP



Four lunar races

Registered on Arbitrum, each with its own market

Touchdown

Next upright working lunar landing

6 competitors

Night Shift

First machine to work through a lunar night

8 competitors

First Tracks

Commercial rover egress and drive

6 competitors


Water Ice

First in-situ surface water ice


4 competitors

Not yet: public betting on the races, an analog prototype test, and revenue. Landed ~8 weeks after the month-2 target; mainnet bets so far are internal tests (0.0127 ETH).

Moon Base Zero: every race, on the Moon

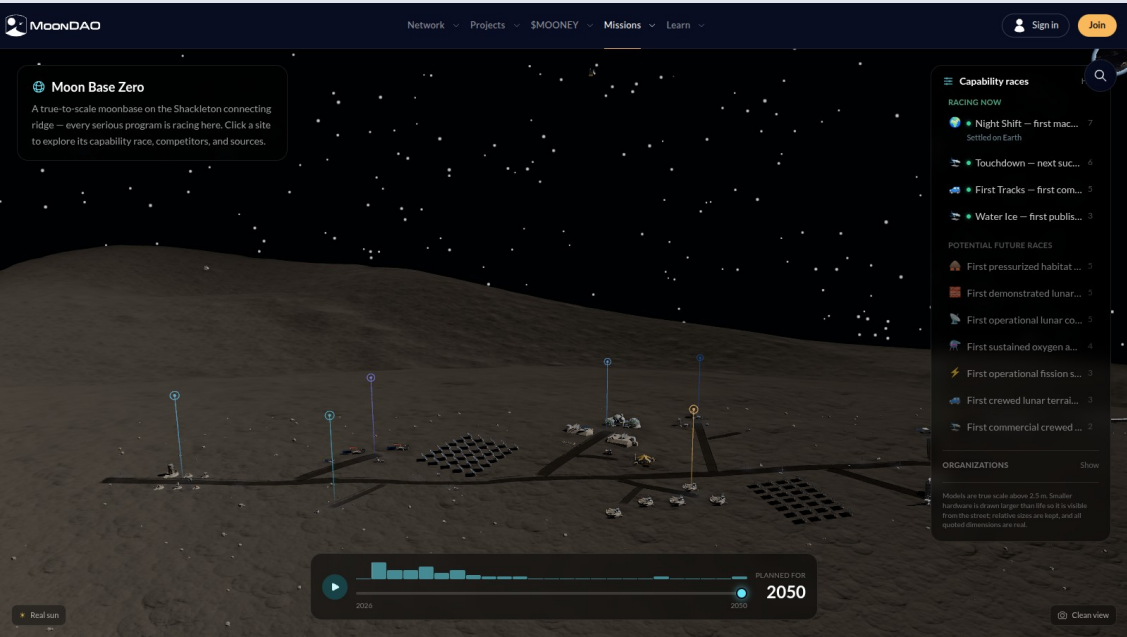

The base on the Shackleton connecting ridge, with the four live races

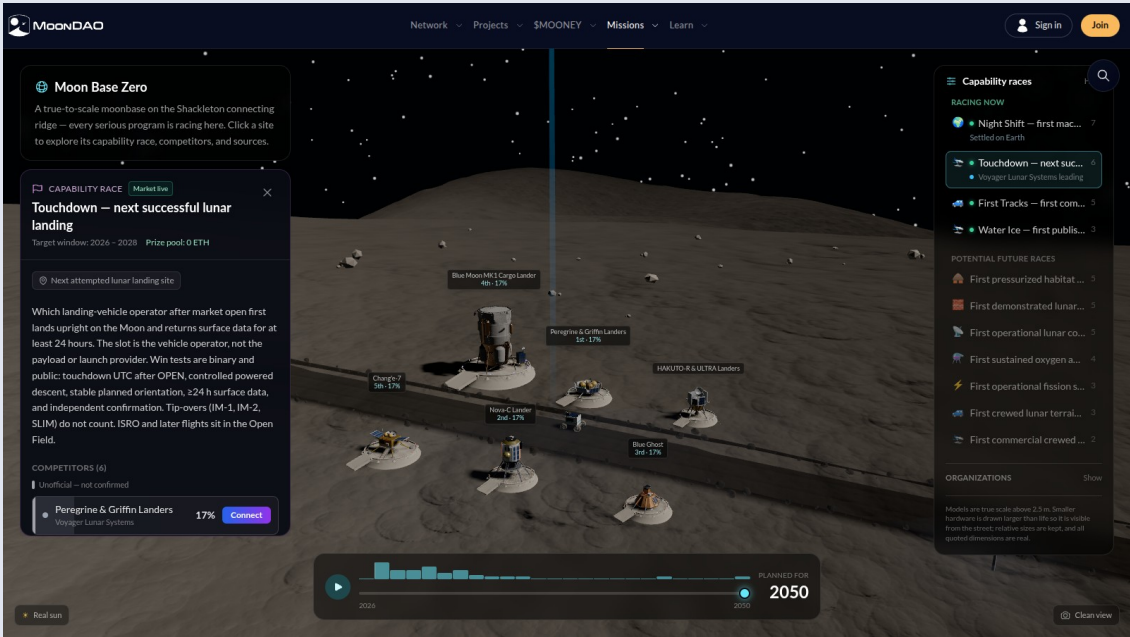

Touchdown race: six landers, rules and live DePrize odds

50 projects

33 organizations

12 capability goals

336 unit tests

First shipped 23 Jul


You chose to keep fundraising for Frank

PATH VOTE • 15–22 JUNE • 31 VOTERS


B • Keep options open, keep fundraising (22 voters)



A • Commit now to a stratospheric balloon (3 voters)



C • Refund contributors (2 voters)



Abstain (4 voters)




Share of 10,444 \$OVERVIEW voting weight

27.39 ETH Raised in total
180 contributions

0.64 ETH Since reopening
9 Jul onward · 21 contributions · 16 wallets


12 Carriers approached
Balloon, suborbital, orbital

Overview Effect Flight — on-chain contributions (Juicebox project 73)

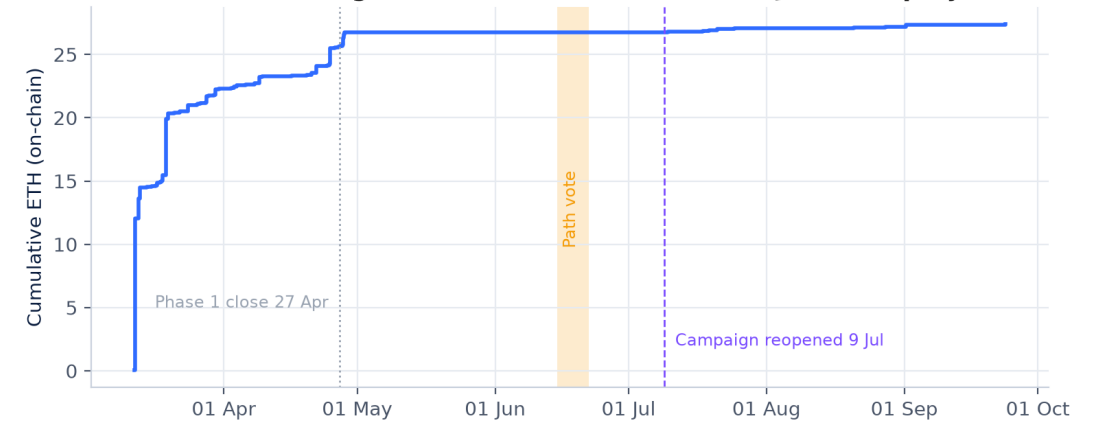

Source: Juicebox V5 terminal 0x2dB6...1846 Pay events, Arbitrum (on-chain only; card/off-chain excluded). As of 7 Oct 2026.

Fastest growth on record, short of target

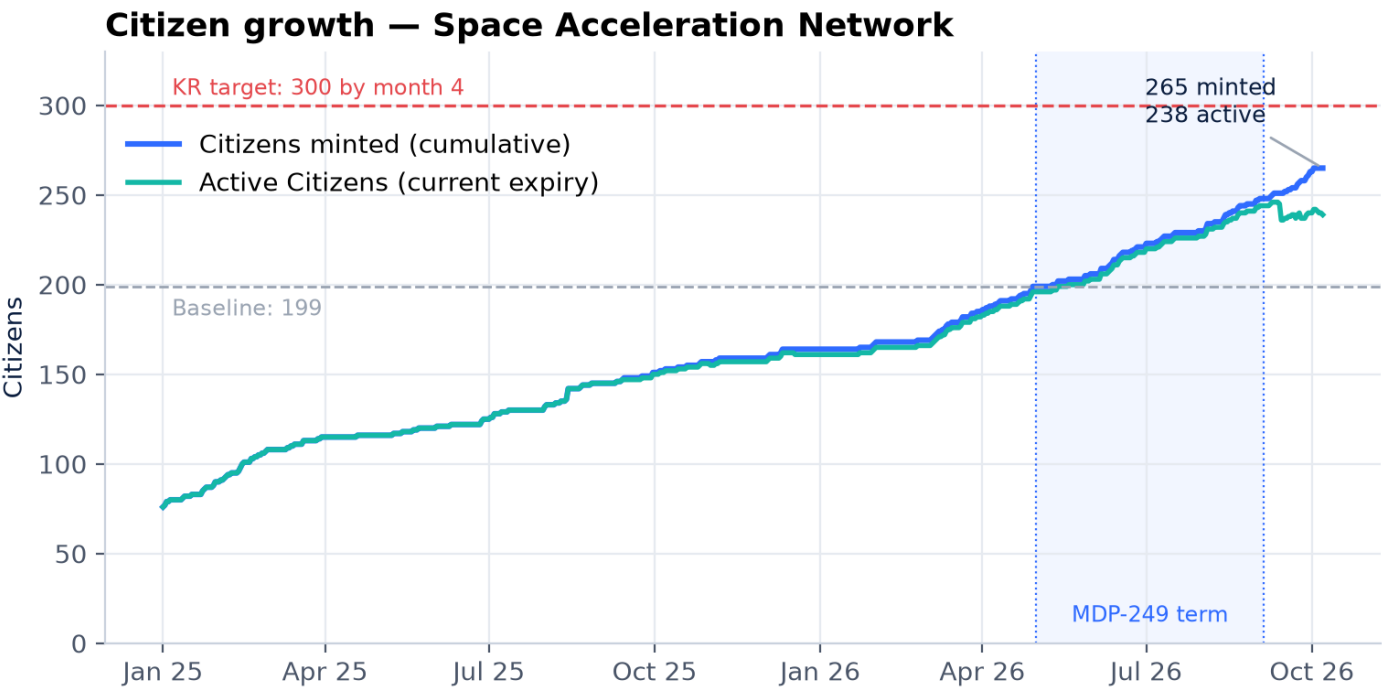

Source: Citizen NFT 0x6E46...E002 (Arbitrum): Transfer-from-zero events and expiresAt(). As of 7 Oct 2026.

199 → 265

Citizens minted

238 active • target 300

20 → 25


Teams

Target 30

New Teams: Habitat Marte, A Heart for Space, USSRC Education Foundation, Geração de Marte, Zephalto

Marketplace beat its target; jobs did not

Team utilization of jobs and marketplace (1 May - 7 Oct 2026) — target 60%

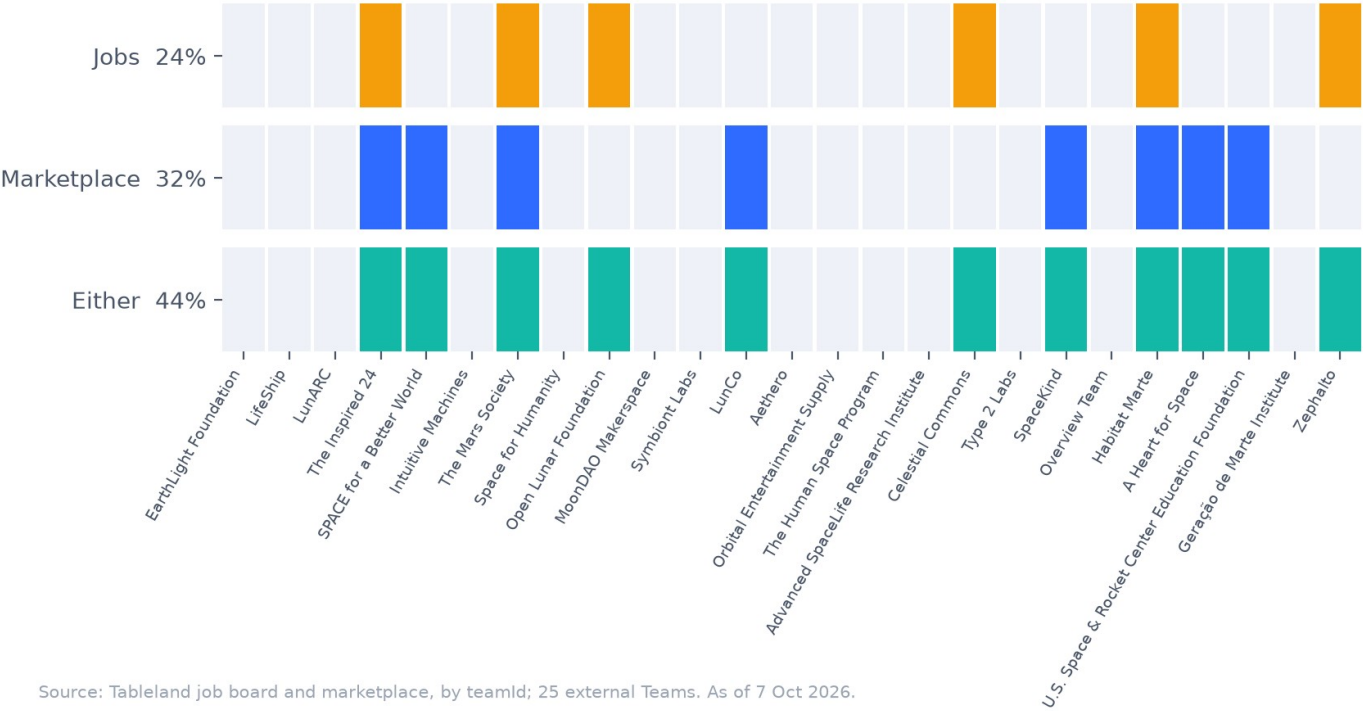

Source: Tableland job board and marketplace, by teamId; 25 external Teams. As of 7 Oct 2026.

17 / 15

Marketplace listings

Target met

7 / 15

Job listings

Target missed

44%

Teams using a service

6 jobs · 8 marketplace · 3 both

30 calls with 21 Teams, two fixes shipped

~30 calls

with 21 Teams

Late May – September • ~2 a week

11 IN THE NETWORK

LifeShip, LunARC, The Inspired 24, Mars Society, The Human Space Program, Celestial Commons, SpaceKind, Habitat Marte, Space Camp USA, Generation Mars Brazil, Zephalto

10 PROSPECTIVE

Including Lonestar (tentatively agreed) and Stardust (whitelisted)

Shipped 1 • Richer, shareable listings

Full descriptions instead of truncated text, a deep link for every listing, and Team pages visible to non-Citizens so links work for anyone.

Asked for by The Inspired 24, Habitat Marte, LunCO

Shipped 2 • Card & bank onramp for purchases

Buyers fund a wallet and buy a listing in one flow without holding crypto. Onboarding no longer steers people to a single provider.

Asked for by Habitat Marte (international payments), LunARC (crypto hurdles)

Most of the operating agenda delivered

Done

- **Project system:** 100% migrated, then Project System v9 (MDP-267)
- **Operational audit:** 14 Aug financial disclosure and burn report, live dashboard
- **GDPR:** Europe opened to browsing; only Citizen creation restricted
- **Realistic Goals:** delivered as the OKRs of the next EB proposal, MDP-271


Partly

- **For-profit arm:** plan and business case drafted, not yet presented
- **Burn reporting:** continuous internal dashboard instead of monthly reports

Not yet

- **Cost reduction:** none; AI-tooling costs rose
- **Election:** nominations and town hall held; Member House vote postponed

On budget: \$132.7k spent of \$132k

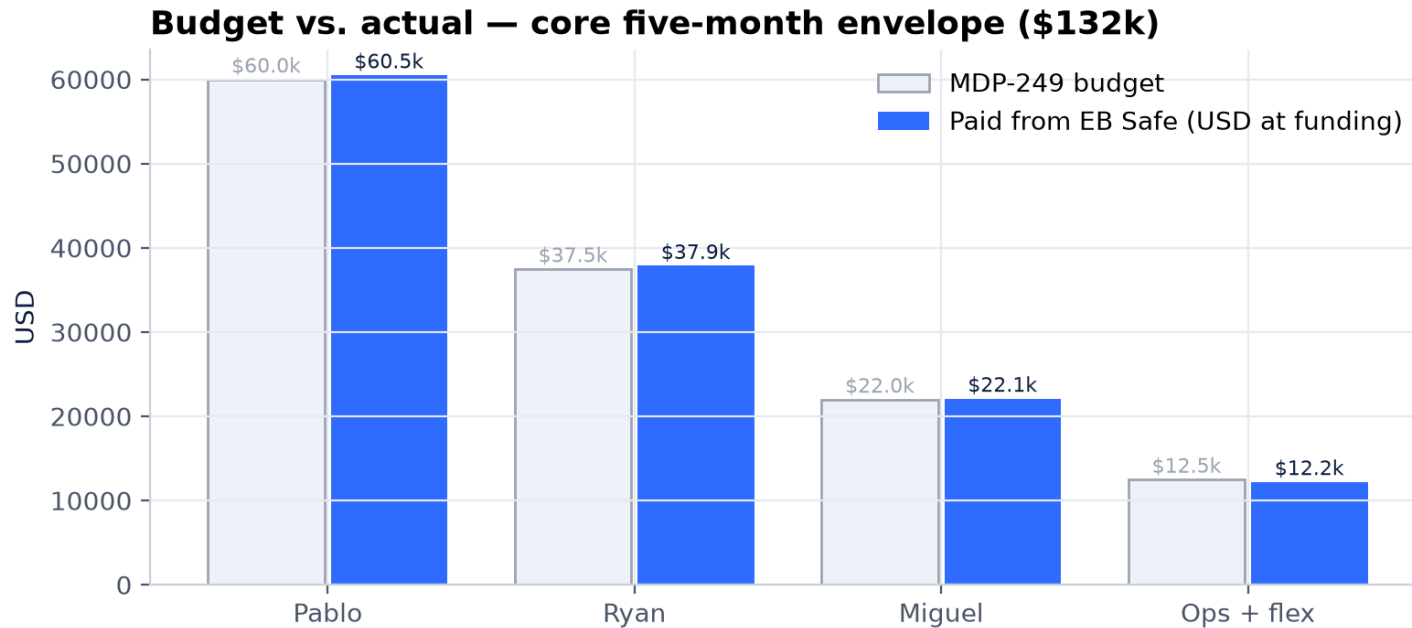

Source: EB Safe 0xdFc3...5291 nonces 36-48; LlamaPay deployments at \$1,843.17/ETH. As of 7 Oct 2026.

+0.6%

vs core budget

\$120.5k payroll + \$12.2k ops & flex

\$0

Bonus paid

Of the \$24k at-risk pool

≈ \$4.3k

On-chain revenue, 12 months

1.67 ETH to the treasury; excludes card/fiat

Provisional grades

OBJECTIVE 1

Frank & DePrize

Meets

Beyond scope on infrastructure; late; no revenue or prototype test yet

OBJECTIVE 2

Network growth

Does not meet

Strong growth and discovery done; Citizen, Team and utilization targets missed

OBJECTIVE 3

Operations

Meets (borderline)

Budget, project system, audit, GDPR done; election and cost cuts not

PERFORMANCE BONUS

\$0 of the \$24,000 pool paid. Of the 10 claimable items, only "project system 100% live" (\$1,000) is clearly met. DePrize launch timing and the lunar challenge are judgment calls for the Executive Leads and the Senate.

What we're carrying into MDP-271

- **Let holders decide.** The path vote gave a clear mandate, but DePrize launched without a seed pool.
- **Growth follows activity.** Our best months had a live campaign; the next term needs a raise.
- **Remove payment friction.** Teams named payments as the blocker; the onramp is now live.
- **Measure cost per outcome.** AI doubled throughput but moved spend from salaries to tooling.

Questions?

Full report, data and every transaction link:
moondao.com/project/131

Next EB proposal:
moondao.com/project/153
